

29 May 2020

Hon Jeffrey Lam Kin-fung, GBG, JP
Chariman
Joint Subcommittee to Monitor the Implementation of
the West Kowloon Cultural District Project
Legislative Council Complex
1 Legislative Council Road
Central, Hong Kong

Dear Jeffrey,

About the project development of the West Kowloon Cultural District

We refer to Hon Tanya Chan's letter dated 24 April 2020 and enquiry at the meeting of the Joint Subcommittee to Monitor the Implementation of the West Kowloon Cultural District Project on 27 April 2020. Hon Tanya Chan asked for the provision of a Gantt Chart/Project Timeline to show the development of different projects at the West Kowloon Cultural District.

In addition to the response the West Kowloon Cultural District Authority provided during the meeting on 27 April 2020, WKCDA has prepared the Gantt Chart as requested. A copy of the chart is attached for your information.

Yours sincerely,




Jeremy Stowe
Chief Projects Officer
West Kowloon Cultural District Authority

Encl.
c.c. Home Affairs Bureau
LegCo Secretariat

WEST KOWLOON CULTURAL DISTRICT HIGH-LEVEL SUMMARY PROGRAMME

Progress as at 30 April 2020

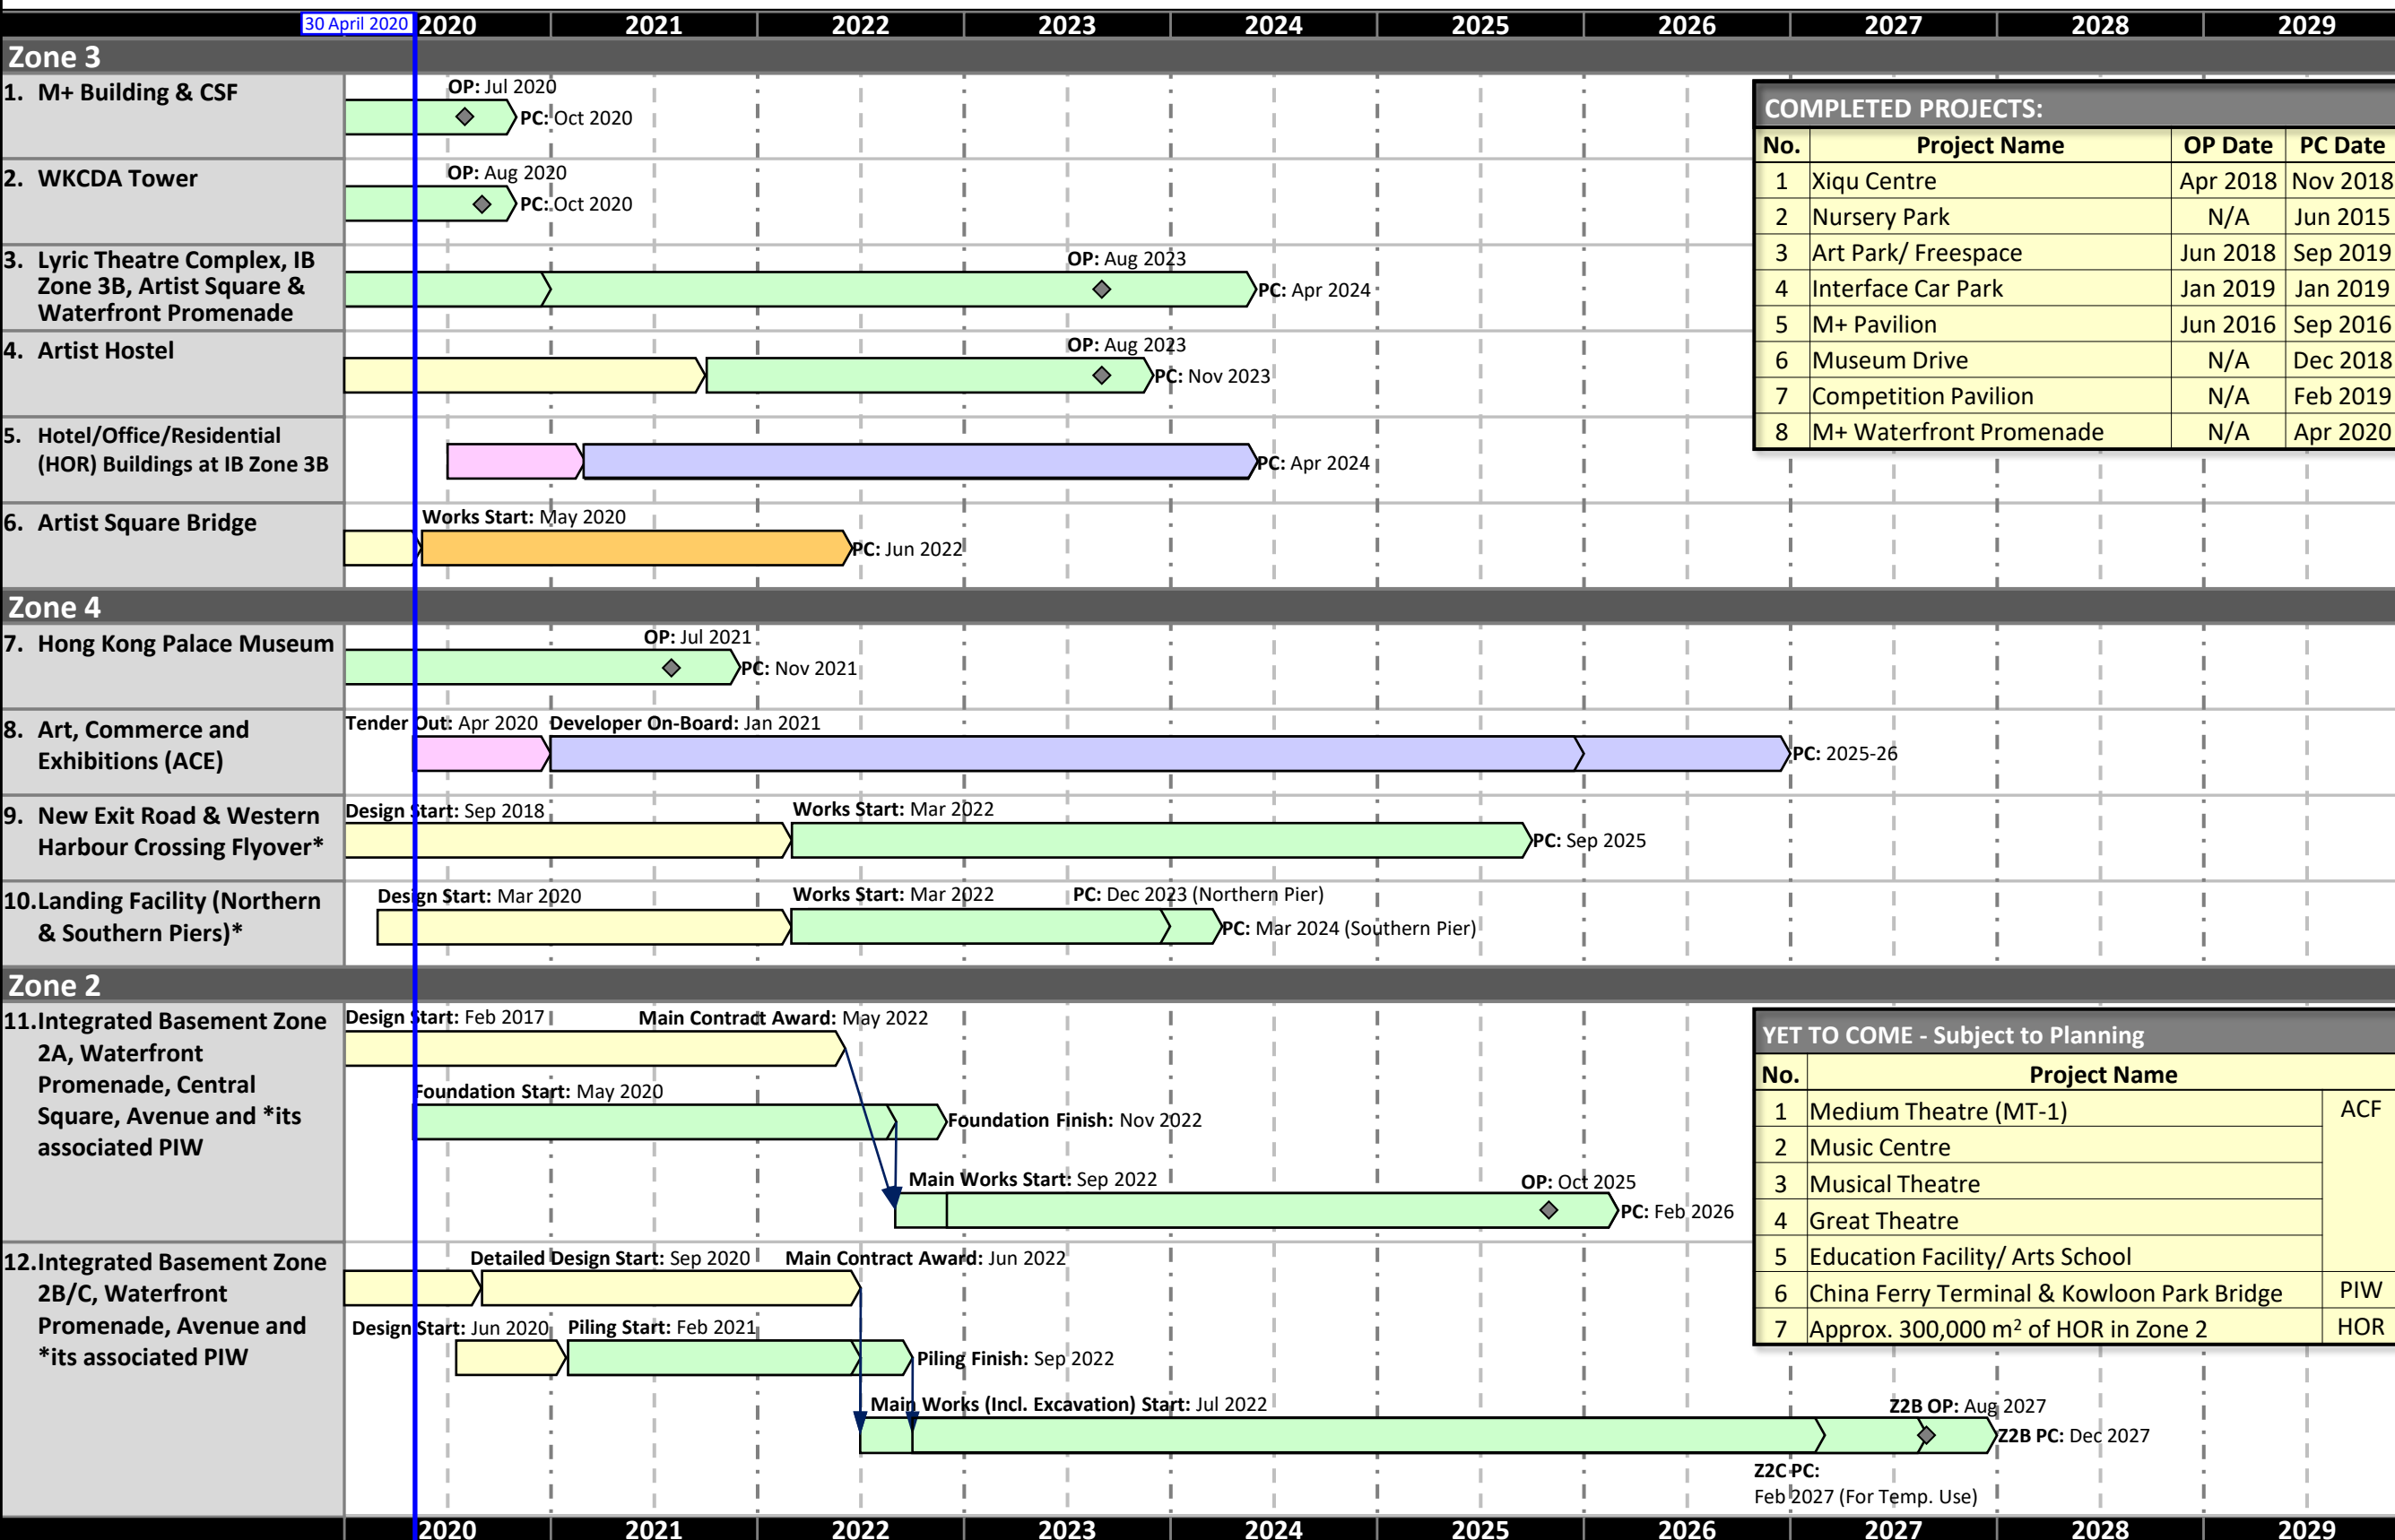

COMPLETED PROJECTS:			
No.	Project Name	OP Date	PC Date
1	Xiqu Centre	Apr 2018	Nov 2018
2	Nursery Park	N/A	Jun 2015
3	Art Park/ Freespace	Jun 2018	Sep 2019
4	Interface Car Park	Jan 2019	Jan 2019
5	M+ Pavilion	Jun 2016	Sep 2016
6	Museum Drive	N/A	Dec 2018
7	Competition Pavilion	N/A	Feb 2019
8	M+ Waterfront Promenade	N/A	Apr 2020

YET TO COME - Subject to Planning		
No.	Project Name	
1	Medium Theatre (MT-1)	ACF
2	Music Centre	
3	Musical Theatre	
4	Great Theatre	
5	Education Facility/ Arts School	PIW
6	China Ferry Terminal & Kowloon Park Bridge	
7	Approx. 300,000 m ² of HOR in Zone 2	HOR

LEGEND:

- Design & Works Contract Procurement
- Design & Build Contract
- Development Tender Procurement (BOT Project)
- Construction
- Obtain Occupation Permit (OP)
- Design, Procurement & Construction (BOT Project)
- OP** Occupation Permit
- PC** Practical Completion
- IB** Integrated Basement
- *** Subject to Government funding availability
